

# S.C.O.U.T. Senior Design: Task Plan, Gantt Chart and WBS

Santa Clara Oceanic Utilities Transmitter · whole team · detailed plan Oct 6 – Oct 18, 2026, all known fall tasks through Jan 15, 2027 · built 2026-10-06 from docs/planning/wbs-tasks.csv (synced from Linear)

## Team and ownership

- **John Ryan Myrdal (GENG)** — field and mechanical: buoy structure, deployment. 41 tasks.
- **Isabella Rodriguez (ECEN)** — hardware: electrical design, power, bench tests. 19 tasks.
- **David Chousal Cantu (CSEN)** — software: firmware, data pipeline, shore station. 10 tasks.
- Advisors: Jes Kuczenski, Hoeseok Yang (ECEN), Navid Shaghaghi.

## Milestones and external deadlines

- **Oct 08, 2026** — Component list delivered; unblocks housing dimensions (*Milestone*)
- **Oct 09, 2026** — Bench parts arrive (assumed Fri) (*Milestone*)
- **Oct 16, 2026** — Phase 1 exit: subsystem bring-up complete (*Milestone*)
- **Oct 18, 2026** — SCU: Undergraduate Programs Project Funding Request due; Gantt chart due (*SCU deadline*)
- **Oct 19, 2026** — Phase 2 starts: system integration (*Milestone*)
- **Nov 25, 2026** — Phase 2 exit (*Milestone*)
- **Jan 15, 2027** — Phase 3 exit: enclosure and waterproofing (*Milestone*)
- **Feb 01, 2027** — SCU: Senior Design Conference registration closes (winter) (*SCU deadline*)


## How to read this

- **WBS:** 1 Project management · 2 Electrical · 3 Firmware & software · 4 Mechanical · 5 Deployment. Each task has a WBS number and, where one exists, its Linear issue.
  - **Pages 2–5:** the Oct 6–18 detail, one block per work area, with dependency arrows. **Then:** the fall overview to Jan 15, and the full table with owner, dates, duration, dependencies, outside constraints and milestones for every task.
  - **Dates:** solid bars use Linear dates. Dashed bars are estimates; the table marks the source of every date. Parts arrival on Fri Oct 9 is an assumption to confirm.
- John Ryan Myrdal (GENG) ■ Isabella Rodriguez (ECE) ■ David Chousal Cantu (CSEN) ■ dashed = estimated dates ■ red outline = blocked / waiting → dependency ◆ milestone
- ◆ external deadline

Outside constraints that drive the plan: SCU funding request and this chart due Oct 18; weekly team meeting (Thu); parts arrival and vendor lead times; shared printer access (industrial printer, Prusa XL, lab printer); advisor and reviewer availability; saltwater soak times of 24 hours to 1 week.

**Detail: Oct 6 – Oct 18, 2026 · WBS 1 / 3 / 5 / Milestones & deadlines**

■ John Ryan Myrdal (GENG)  
 ■ Isabella Rodriguez (ECE)  
 ■ David Chousal Cantu (CSEN)  
 ■ dashed = estimated dates  
 ■ red outline = blocked / waiting  
 → dependency  
 ◆ milestone  
◆ external deadline

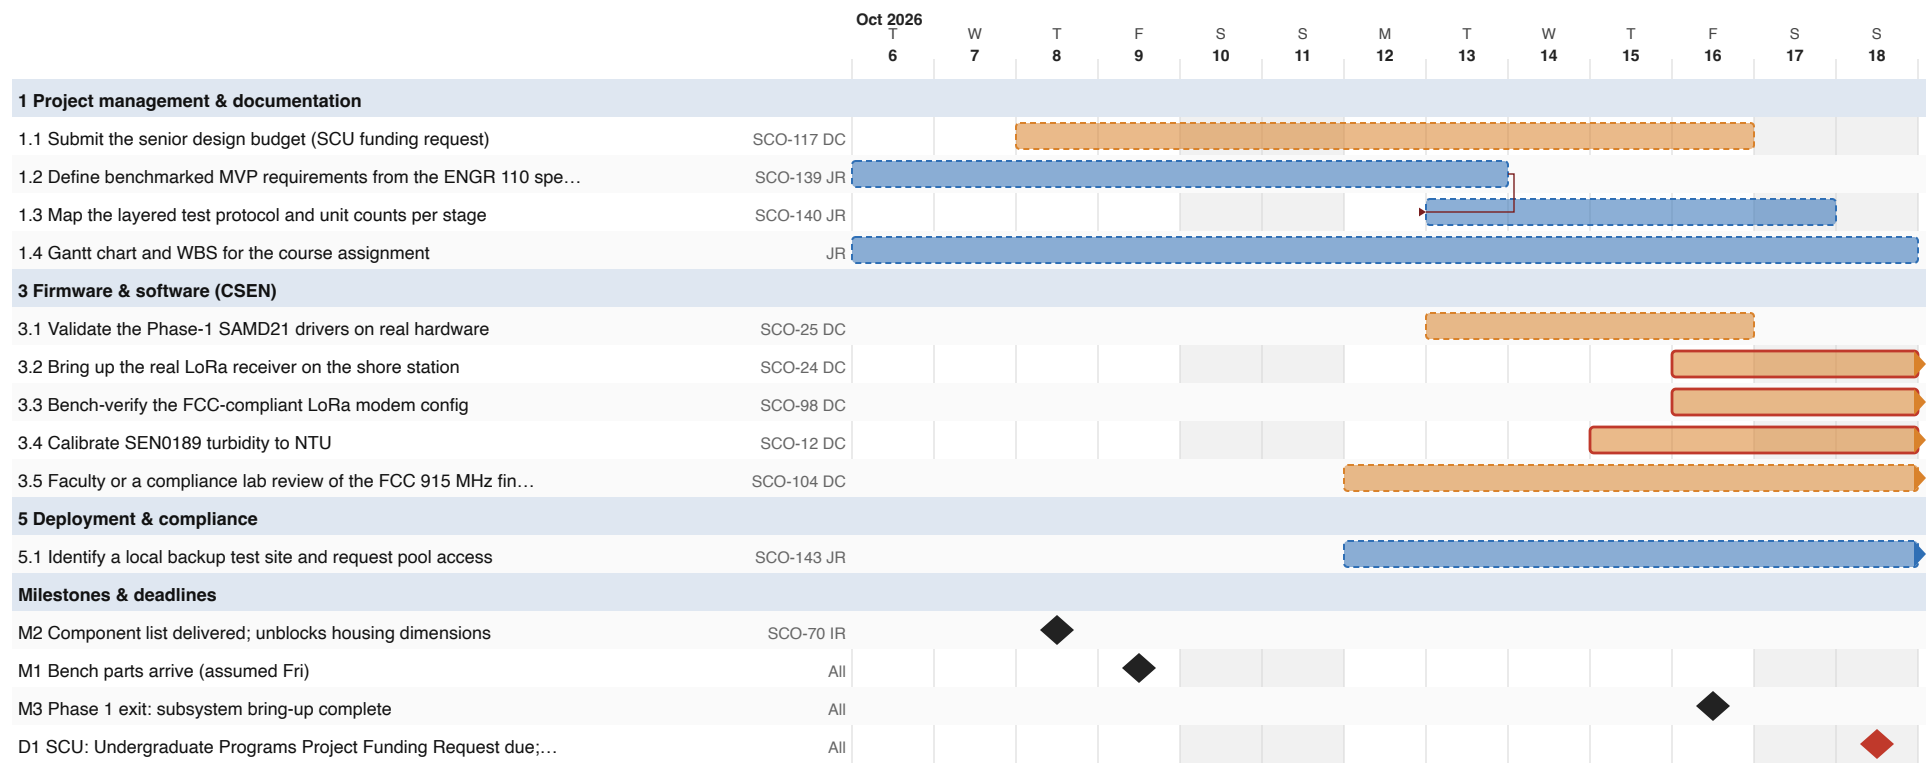

**Detail: Oct 6 – Oct 18, 2026 · WBS 2**

John Ryan Myrdal (GENG)

■ Isabella Rodriguez (ECE)

David Chousal Cantu (CSEN)


■ dashed = estimated dates

 red outline = blocked / waiting

→ dependency


◆ milestone

- ◆ external deadline

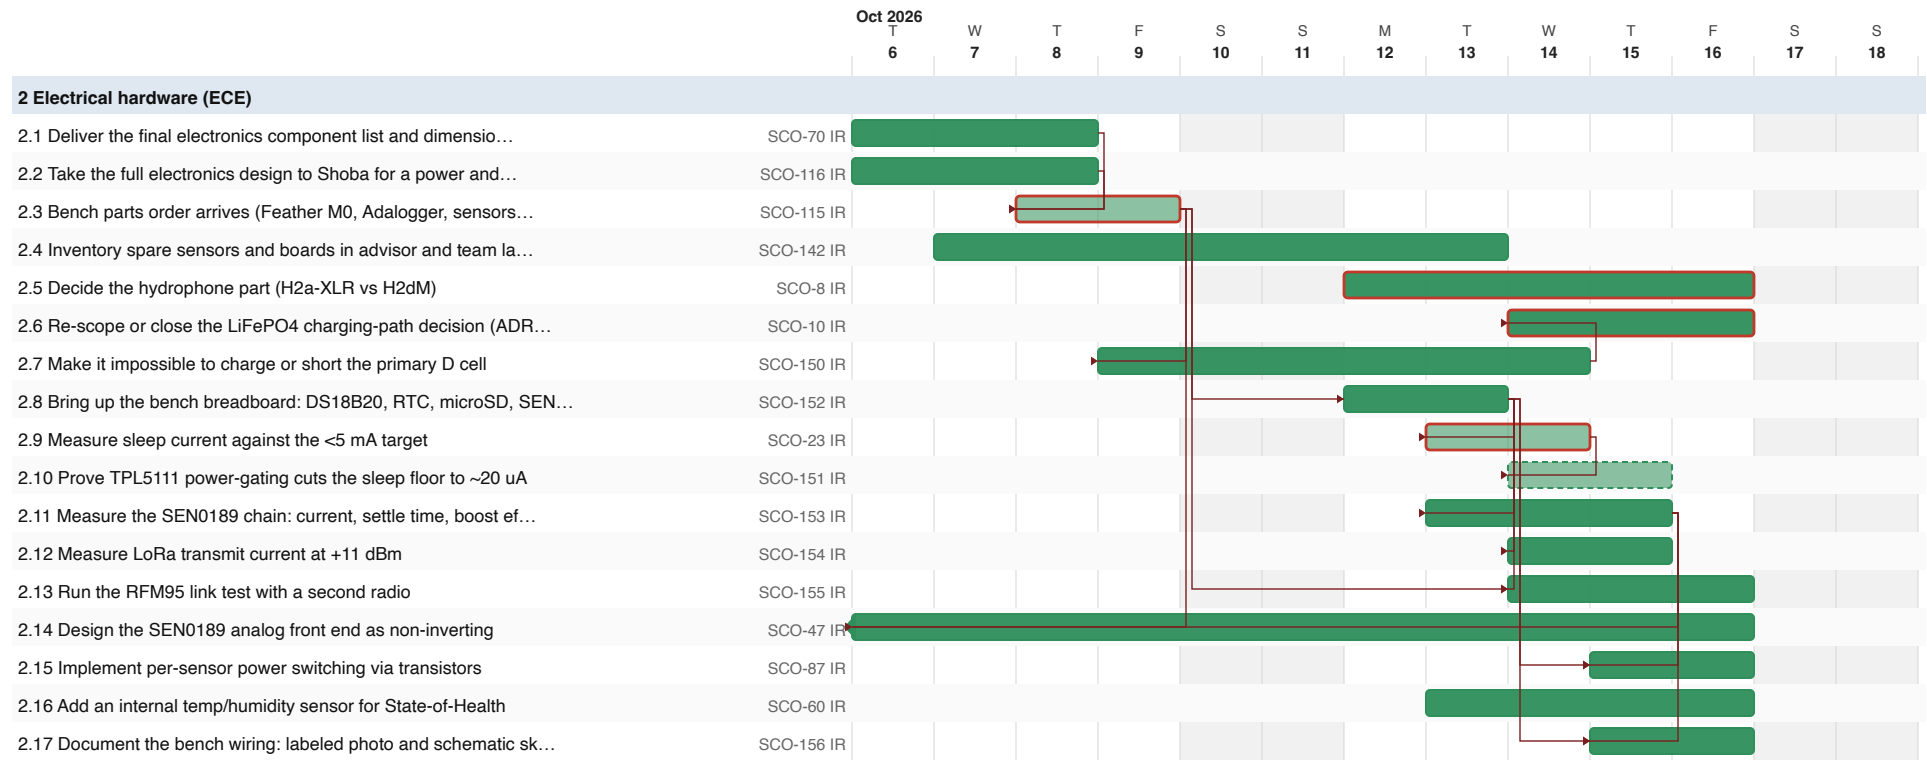

**Detail: Oct 6 – Oct 18, 2026 · WBS 4**

■ John Ryan Myrdal (GENG)  
 ■ Isabella Rodriguez (ECE)  
 ■ David Chousal Cantu (CSEN)  
 ■ dashed = estimated dates  
  red outline = blocked / waiting  
 → dependency  
 ◆ milestone  
◆ external deadline

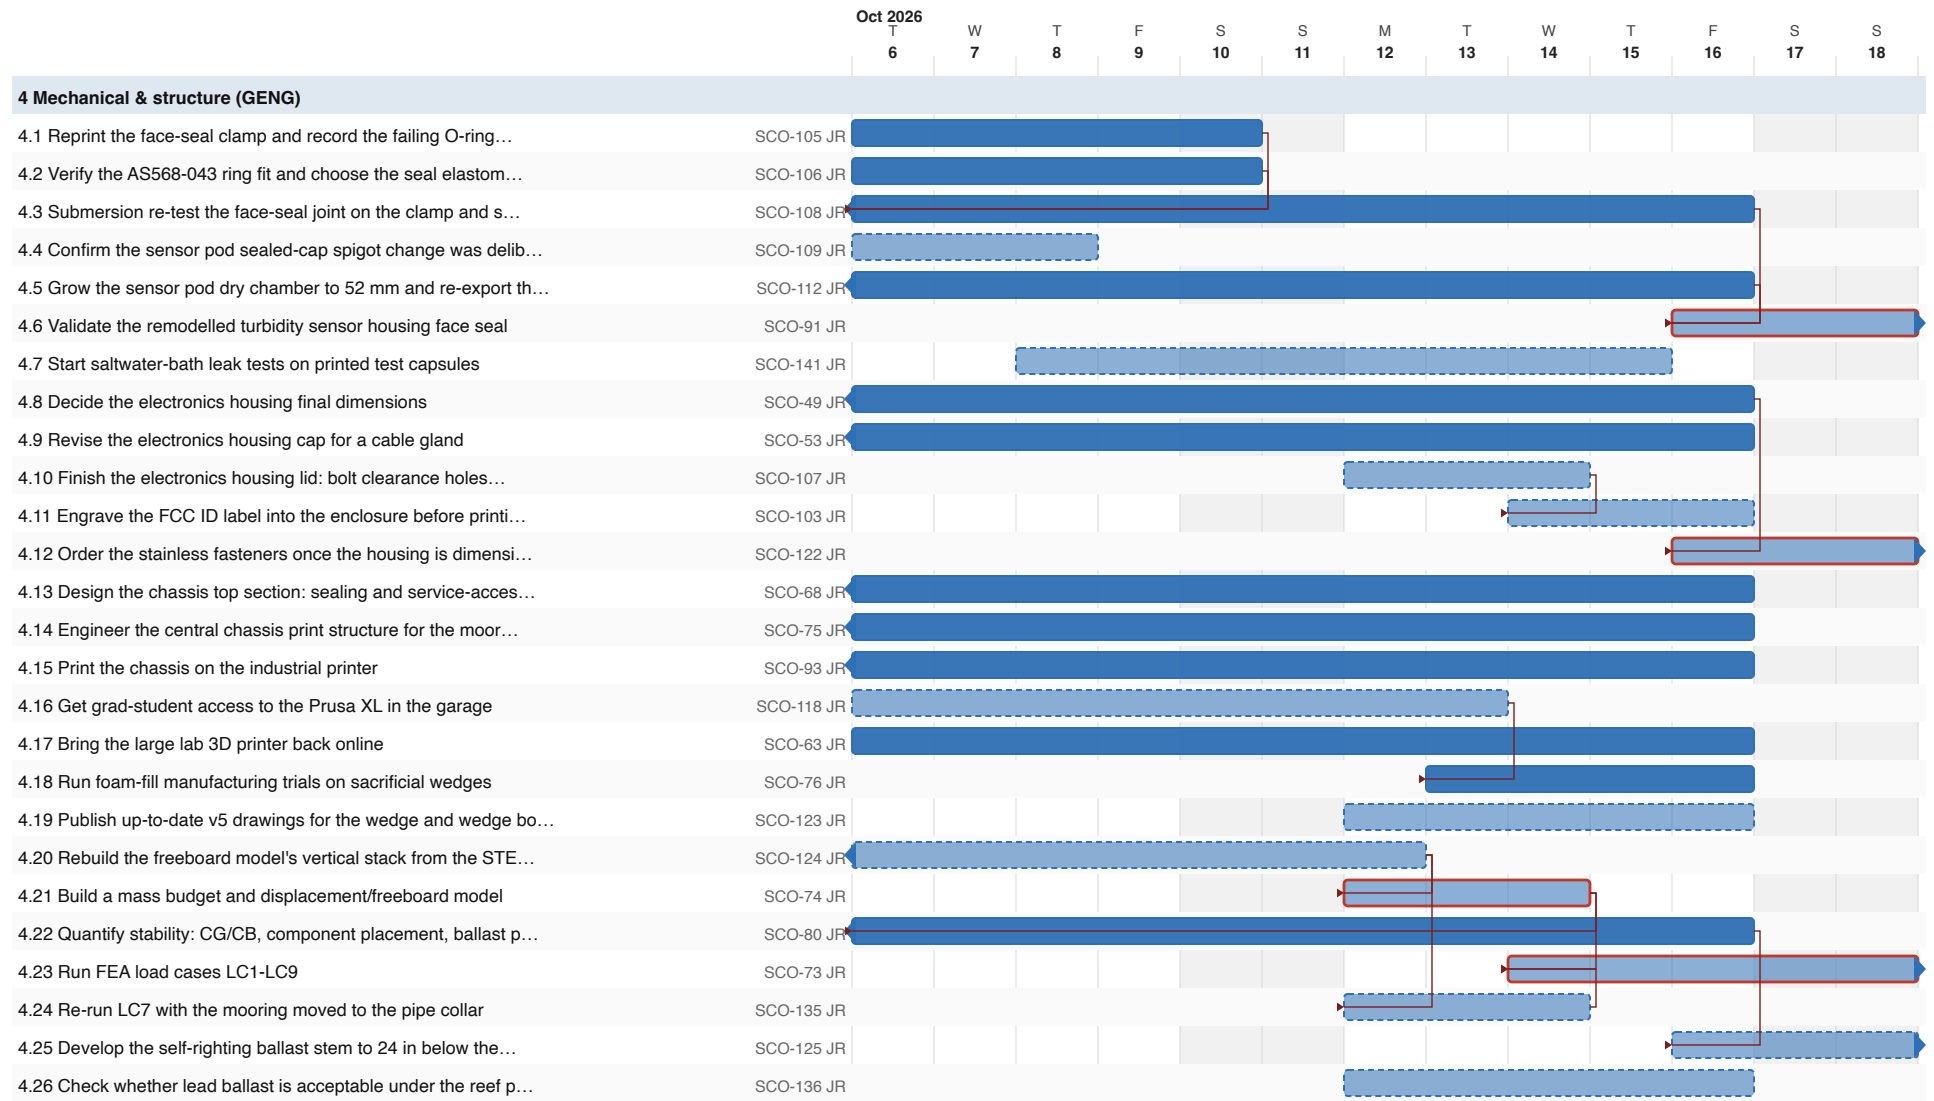


**Detail: Oct 6 – Oct 18, 2026 · WBS**

■ John Ryan Myrdal (GENG)  
 ■ Isabella Rodriguez (ECE)  
 ■ David Chousal Cantu (CSEN)  
 ■ dashed = estimated dates  
  red outline = blocked / waiting  
 → dependency  
 ◆ milestone  
◆ external deadline




### Fall overview: Oct 2026 – Jan 2027 (week columns)

■ John Ryan Myrdal (GENG)  
 ■ Isabella Rodriguez (ECE)  
 ■ David Chousal Cantu (CSEN)  
 ■ dashed = estimated dates  
  red outline = blocked / waiting  
 → dependency  
 ◆ milestone  
 ◆ external deadline

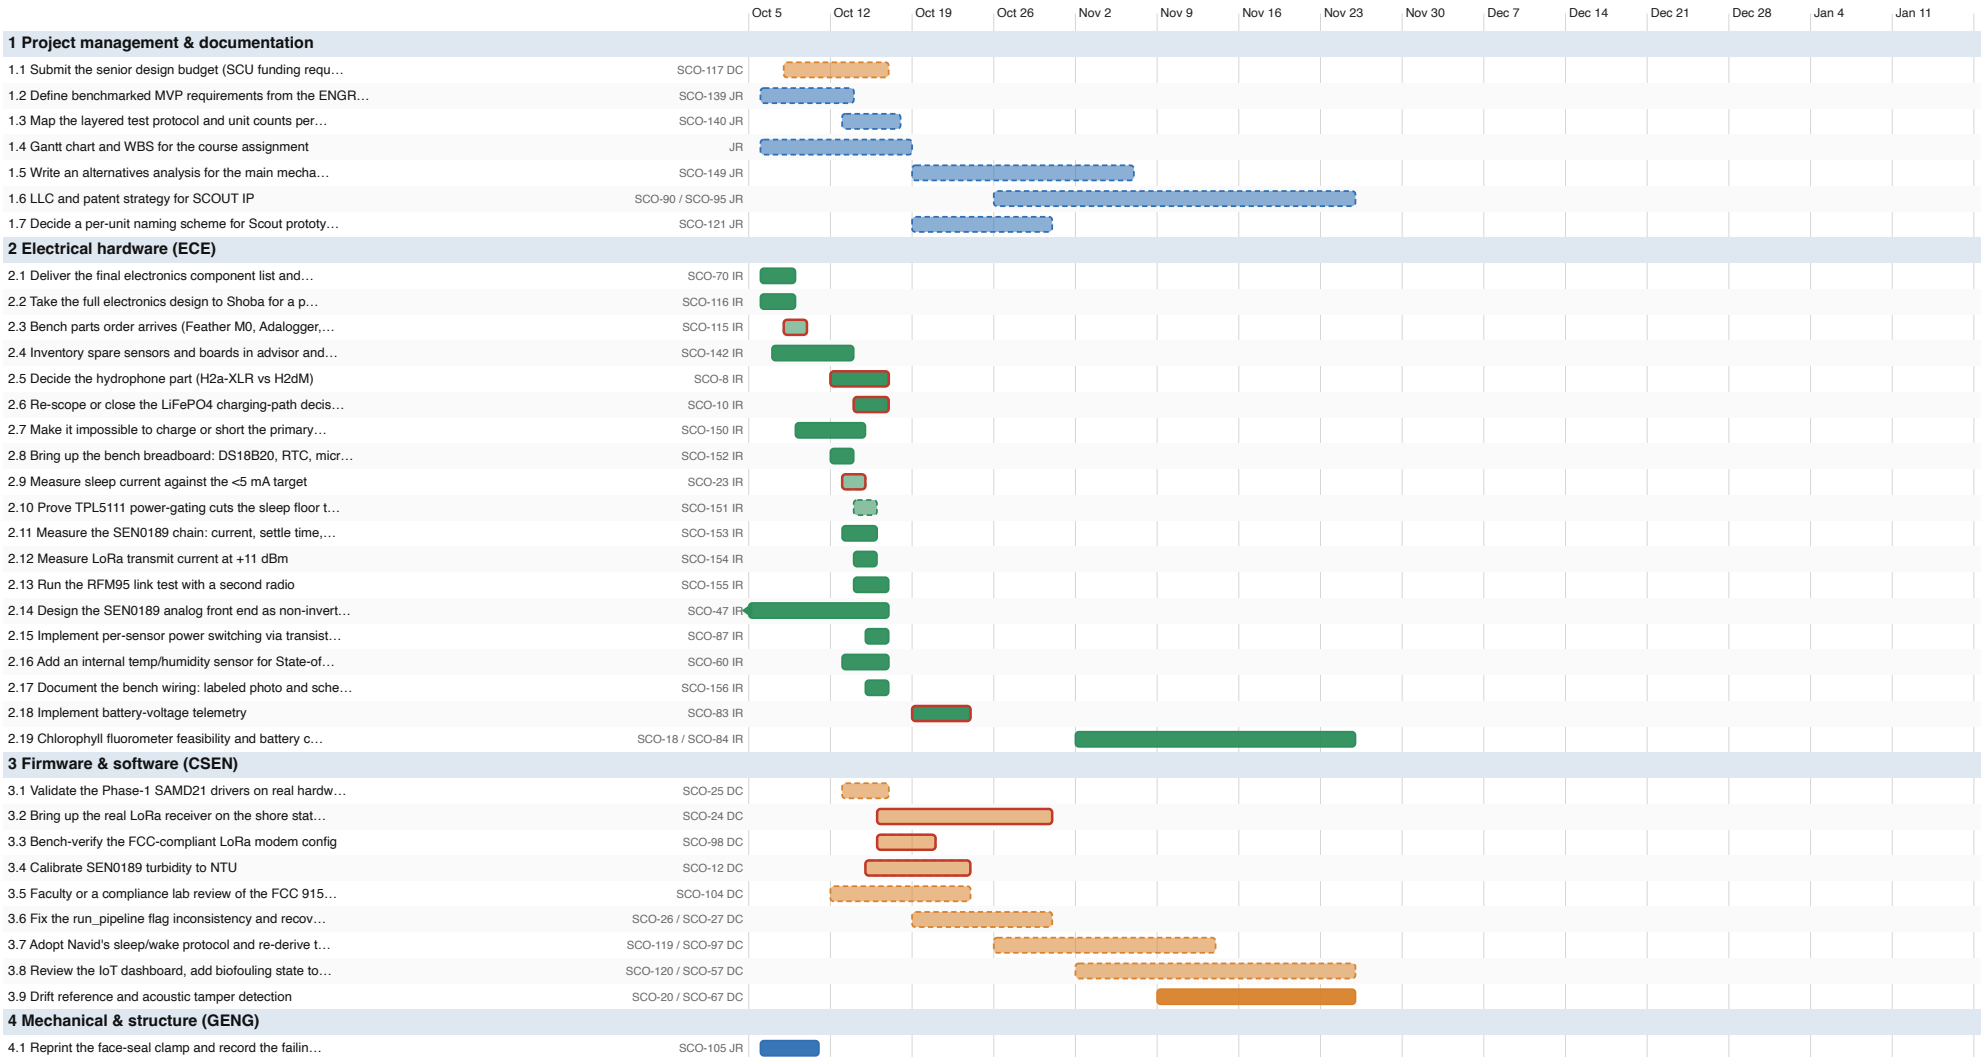

**Fall overview: Oct 2026 – Jan 2027 (week columns) (cont.)**

■ John Ryan Myrdal (GENG)  
 ■ Isabella Rodriguez (ECE)  
 ■ David Chousal Cantu (CSEN)  
  dashed = estimated dates  
  red outline = blocked / waiting  
 → dependency  
 ◆ milestone  
◆ external deadline

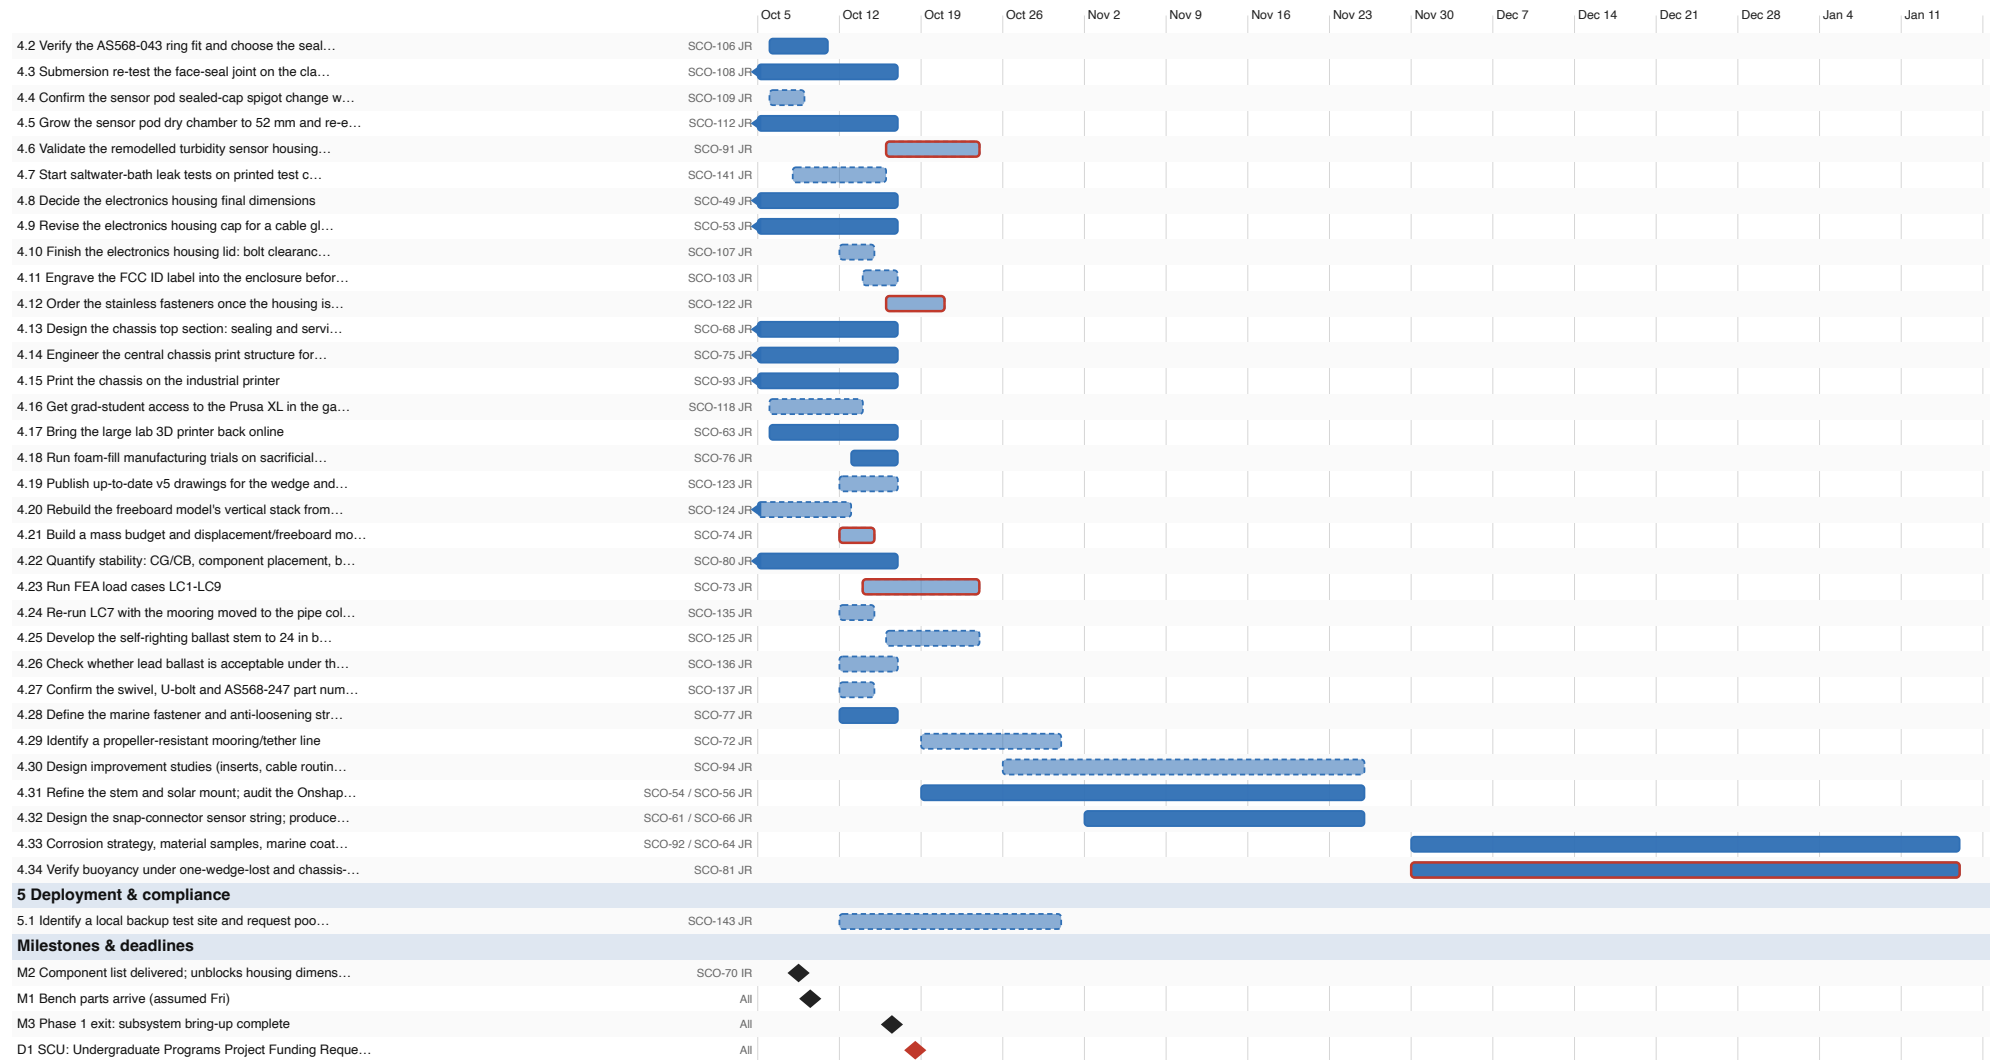

**Fall overview: Oct 2026 – Jan 2027 (week columns) (cont.)**

■ John Ryan Myrdal (GENG)

■ Isabella Rodriguez (ECE)

David Chousal Cantu (CSEN)

 dashed = estimated dates

 red outline = blocked / waiting

→ dependency

- ◆ milestone

- external deadline



## Task table (all columns)

| WBS                                  | Linear          | Task                                                                                | Owner    | Phase   | Status           | Start      | End        | Days | Depends on       | Outside constraint                                                                                                                  | Milestone / deadline      | Date source |
|--------------------------------------|-----------------|-------------------------------------------------------------------------------------|----------|---------|------------------|------------|------------|------|------------------|-------------------------------------------------------------------------------------------------------------------------------------|---------------------------|-------------|
| 1 Project management & documentation |                 |                                                                                     |          |         |                  |            |            |      |                  |                                                                                                                                     |                           |             |
| 1.1                                  | SCO-117         | Submit the senior design budget (SCU funding request)                               | David    | Phase 1 | Todo             | 2026-10-08 | 2026-10-16 | 9    | SCO-116          | Lab budget was due the week of 2026-09-28 (overdue); SCU funding request deadline Oct 18; must match the parts order                | Funding request submitted | estimated   |
| 1.2                                  | SCO-139         | Define benchmarked MVP requirements from the ENGR 110 specs                         | John     | Phase 1 | Todo             | 2026-10-06 | 2026-10-13 | 8    |                  | Advisor asked for measurable benchmarks (2026-09-30 meeting)                                                                        |                           | estimated   |
| 1.3                                  | SCO-140         | Map the layered test protocol and unit counts per stage                             | John     | Phase 1 | Todo             | 2026-10-13 | 2026-10-17 | 5    | SCO-139          | Advisor asked for a layered test plan (2026-09-30 meeting)                                                                          | Test protocol drafted     | estimated   |
| 1.4                                  |                 | Gantt chart and WBS for the course assignment                                       | John     | Phase 1 | In Progress      | 2026-10-06 | 2026-10-18 | 13   |                  | Course deadline Oct 18; whole team                                                                                                  | Gantt submitted           | derived     |
| 1.5                                  | SCO-149         | Write an alternatives analysis for the main mechanical choices                      | John     | Phase 2 | Backlog          | 2026-10-19 | 2026-11-06 | 19   |                  |                                                                                                                                     |                           | estimated   |
| 1.6                                  | SCO-90 / SCO-95 | LLC and patent strategy for SCOUT IP                                                | John     | Phase 2 | Backlog          | 2026-10-26 | 2026-11-25 | 31   |                  | Possible advisor or university IP office input                                                                                      |                           | estimated   |
| 1.7                                  | SCO-121         | Decide a per-unit naming scheme for Scout prototypes                                | John     | Phase 2 | Backlog          | 2026-10-19 | 2026-10-30 | 12   |                  | Unassigned in Linear; needs team agreement                                                                                          |                           | estimated   |
| 2 Electrical hardware (ECE)          |                 |                                                                                     |          |         |                  |            |            |      |                  |                                                                                                                                     |                           |             |
| 2.1                                  | SCO-70          | Deliver the final electronics component list and dimensions                         | Isabella | Phase 1 | Todo             | 2026-10-06 | 2026-10-08 | 3    |                  | Overdue since 2026-09-04; blocks housing dimensions                                                                                 | Component list final      | Linear      |
| 2.2                                  | SCO-116         | Take the full electronics design to Shoba for a power and solar review              | Isabella | Phase 1 | Todo             | 2026-10-06 | 2026-10-08 | 3    |                  | Shoba's availability; Dr. Yang review follows                                                                                       | Design review complete    | Linear      |
| 2.3                                  | SCO-115         | Bench parts order arrives (Feather M0, Adalogger, sensors, boost, TPL5111)          | Isabella | Phase 1 | Waiting on Parts | 2026-10-08 | 2026-10-09 | 2    | SCO-70, SCO-116  | Vendor shipping; ordered through Dr. Krishnan 2026-10-05; arrival date assumed                                                      | Parts arrive              | estimated   |
| 2.4                                  | SCO-142         | Inventory spare sensors and boards in advisor and team labs                         | Isabella | Phase 1 | Todo             | 2026-10-07 | 2026-10-13 | 7    |                  | Needs advisor and lab access                                                                                                        |                           | Linear      |
| 2.5                                  | SCO-8           | Decide the hydrophone part (H2a-XLR vs H2dM)                                        | Isabella | Phase 1 | Needs Decision   | 2026-10-12 | 2026-10-16 | 5    |                  | Hydrophone not in the bench order                                                                                                   | Decision recorded         | Linear      |
| 2.6                                  | SCO-10          | Re-scope or close the LiFePO4 charging-path decision (ADR-0002)                     | Isabella | Phase 1 | Needs Decision   | 2026-10-14 | 2026-10-16 | 3    | SCO-150          | Overtaken if ADR-0007 (Li-SOC12 primary cell) is accepted                                                                           | Decision recorded         | Linear      |
| 2.7                                  | SCO-150         | Make it impossible to charge or short the primary D cell                            | Isabella | Phase 1 | Todo             | 2026-10-09 | 2026-10-14 | 6    | SCO-115          | Fire-safety layers must exist before any real cell; bench uses a current-limited supply                                             |                           | Linear      |
| 2.8                                  | SCO-152         | Bring up the bench breadboard: DS18B20, RTC, microSD, SEN0189 wiring                | Isabella | Phase 1 | Todo             | 2026-10-12 | 2026-10-13 | 2    | SCO-115          | Needs the parts to arrive; bench supply and uA meter reserved                                                                       | Bench bring-up complete   | Linear      |
| 2.9                                  | SCO-23          | Measure sleep current against the <5 mA target                                      | Isabella | Phase 1 | Waiting on Parts | 2026-10-13 | 2026-10-14 | 2    | SCO-152          | uA-range multimeter; 3.6 V current-limited supply                                                                                   |                           | estimated   |
| 2.10                                 | SCO-151         | Prove TPL5111 power-gating cuts the sleep floor to ~20 uA                           | Isabella | Phase 1 | Todo             | 2026-10-14 | 2026-10-15 | 2    | SCO-23           | Firmware cold-boot support from David (SCO-25)                                                                                      |                           | estimated   |
| 2.11                                 | SCO-153         | Measure the SEN0189 chain: current, settle time, boost efficiency, inrush, polarity | Isabella | Phase 1 | Todo             | 2026-10-13 | 2026-10-15 | 3    | SCO-152          | Oscilloscope for inrush                                                                                                             |                           | Linear      |
| 2.12                                 | SCO-154         | Measure LoRa transmit current at +11 dBm                                            | Isabella | Phase 1 | Todo             | 2026-10-14 | 2026-10-15 | 2    | SCO-152          | 1 ohm shunt; re-check after SCO-98                                                                                                  |                           | Linear      |
| 2.13                                 | SCO-155         | Run the RFM95 link test with a second radio                                         | Isabella | Phase 1 | Todo             | 2026-10-14 | 2026-10-16 | 3    | SCO-152, SCO-115 | Second radio is not in the 10-05 order; lab stock or a new order                                                                    | Radio link proven         | Linear      |
| 2.14                                 | SCO-47          | Design the SEN0189 analog front end as non-inverting                                | Isabella | Phase 1 | In Progress      | 2026-09-01 | 2026-10-16 | 46   | SCO-115, SCO-153 | Polarity must not invert; bench check after parts arrive; Design started 2026-09-01; bench verification follows SCO-115 and SCO-153 |                           | Linear      |
| 2.15                                 | SCO-87          | Implement per-sensor power switching via transistors                                | Isabella | Phase 1 | Todo             | 2026-10-15 | 2026-10-16 | 2    | SCO-152, SCO-153 | V1-required on a primary cell                                                                                                       |                           | Linear      |
| 2.16                                 | SCO-60          | Add an internal temp/humidity sensor for State-of-Health                            | Isabella | Phase 1 | Todo             | 2026-10-13 | 2026-10-16 | 4    |                  |                                                                                                                                     |                           | Linear      |
| 2.17                                 | SCO-156         | Document the bench wiring: labeled photo and schematic sketch to /hardware          | Isabella | Phase 1 | Todo             | 2026-10-15 | 2026-10-16 | 2    | SCO-152, SCO-153 | Phase 1 exit item                                                                                                                   | Phase 1 hardware exit     | Linear      |

|                                            |                           |                                                                                             |          |         |                  |            |            |    |                  |                                                                                                                                               |                               |           |
|--------------------------------------------|---------------------------|---------------------------------------------------------------------------------------------|----------|---------|------------------|------------|------------|----|------------------|-----------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-----------|
| 2.18                                       | SCO-83                    | Implement battery-voltage telemetry                                                         | Isabella | Phase 2 | Blocked          | 2026-10-19 | 2026-10-23 | 5  | SCO-10           | Depends on the battery chemistry decision                                                                                                     |                               | Linear    |
| 2.19                                       | SCO-18 / SCO-84           | Chlorophyll fluorometer feasibility and battery connector polarity check                    | Isabella | Phase 2 | Deferred         | 2026-11-02 | 2026-11-25 | 24 |                  | Deferred in Linear; not this version                                                                                                          |                               | Linear    |
| <b>3 Firmware &amp; software (CSEN)</b>    |                           |                                                                                             |          |         |                  |            |            |    |                  |                                                                                                                                               |                               |           |
| 3.1                                        | SCO-25                    | Validate the Phase-1 SAMD21 drivers on real hardware                                        | David    | Phase 1 | Todo             | 2026-10-13 | 2026-10-16 | 4  | SCO-115, SCO-152 | Needs the Feather M0 from the bench order                                                                                                     | Drivers validated on hardware | estimated |
| 3.2                                        | SCO-24                    | Bring up the real LoRa receiver on the shore station                                        | David    | Phase 1 | Waiting on Parts | 2026-10-16 | 2026-10-30 | 15 | SCO-115, SCO-155 | Linear due 10-16 moved to 10-30: shore parts (Feather S3, LoRa module) are not ordered yet                                                    |                               | estimated |
| 3.3                                        | SCO-98                    | Bench-verify the FCC-compliant LoRa modem config                                            | David    | Phase 1 | Blocked          | 2026-10-16 | 2026-10-20 | 5  | SCO-155          | Config is merged; only bench verification remains                                                                                             |                               | estimated |
| 3.4                                        | SCO-12                    | Calibrate SEN0189 turbidity to NTU                                                          | David    | Phase 1 | Blocked          | 2026-10-15 | 2026-10-23 | 9  | SCO-153          | Formazin standards and a nephelometer method; Linear due 10-16 moved to 10-23                                                                 |                               | estimated |
| 3.5                                        | SCO-104                   | Faculty or a compliance lab review of the FCC 915 MHz findings                              | David    | Phase 1 | Todo             | 2026-10-12 | 2026-10-23 | 12 |                  | Reviewer availability                                                                                                                         |                               | estimated |
| 3.6                                        | SCO-26 / SCO-27           | Fix the run_pipeline flag inconsistency and recover the missing Sesoko recording            | David    | Phase 2 | Backlog          | 2026-10-19 | 2026-10-30 | 12 |                  | Recording may need the original data source                                                                                                   |                               | estimated |
| 3.7                                        | SCO-119 / SCO-97          | Adopt Navid's sleep/wake protocol and re-derive the packet ceiling                          | David    | Phase 2 | Backlog          | 2026-10-26 | 2026-11-13 | 19 | SCO-98           |                                                                                                                                               |                               | estimated |
| 3.8                                        | SCO-120 / SCO-57 / SCO-58 | Review the IoT dashboard, add biofouling state to the Fleet page, improve the PNG dashboard | David    | Phase 2 | Backlog          | 2026-11-02 | 2026-11-25 | 24 | SCO-24           |                                                                                                                                               | Phase 2 software exit         | estimated |
| 3.9                                        | SCO-20 / SCO-67           | Drift reference and acoustic tamper detection                                               | David    | Phase 2 | Deferred         | 2026-11-09 | 2026-11-25 | 17 |                  | Deferred in Linear; not this version                                                                                                          |                               | Linear    |
| <b>4 Mechanical &amp; structure (GENG)</b> |                           |                                                                                             |          |         |                  |            |            |    |                  |                                                                                                                                               |                               |           |
| 4.1                                        | SCO-105                   | Reprint the face-seal clamp and record the failing O-ring tolerance                         | John     | Phase 1 | Todo             | 2026-10-06 | 2026-10-10 | 5  |                  | Printer access                                                                                                                                |                               | Linear    |
| 4.2                                        | SCO-106                   | Verify the AS568-043 ring fit and choose the seal elastomer before ordering                 | John     | Phase 1 | Todo             | 2026-10-06 | 2026-10-10 | 5  |                  | Decision: silicone elastomer (2026-09-08)                                                                                                     |                               | Linear    |
| 4.3                                        | SCO-108                   | Submersion re-test the face-seal joint on the clamp and sensor pod                          | John     | Phase 1 | In Progress      | 2026-10-01 | 2026-10-16 | 16 | SCO-105, SCO-106 | 24 hr soaks; RR-14 result 10-07; RR-15 (6 bolts) after; Coupon re-tests (RR-14, RR-15) run now; the clamp re-test follows SCO-105 and SCO-106 | Face seal passes a 24 hr soak | Linear    |
| 4.4                                        | SCO-109                   | Confirm the sensor pod sealed-cap spigot change was deliberate                              | John     | Phase 1 | Todo             | 2026-10-06 | 2026-10-08 | 3  |                  |                                                                                                                                               |                               | estimated |
| 4.5                                        | SCO-112                   | Grow the sensor pod dry chamber to 52 mm and re-export the penetration and flood chamber    | John     | Phase 1 | In Progress      | 2026-09-14 | 2026-10-16 | 33 |                  | Epoxy-potted lead penetration                                                                                                                 |                               | Linear    |
| 4.6                                        | SCO-91                    | Validate the remodelled turbidity sensor housing face seal                                  | John     | Phase 1 | Blocked          | 2026-10-16 | 2026-10-23 | 8  | SCO-108, SCO-112 |                                                                                                                                               |                               | estimated |
| 4.7                                        | SCO-141                   | Start saltwater-bath leak tests on printed test capsules                                    | John     | Phase 1 | Todo             | 2026-10-08 | 2026-10-15 | 8  |                  | 1 week soak at about 35 ppt                                                                                                                   |                               | estimated |
| 4.8                                        | SCO-49                    | Decide the electronics housing final dimensions                                             | John     | Phase 1 | In Progress      | 2026-08-18 | 2026-10-16 | 60 | SCO-70           | Needs Isabella's component list; drawing DFM Assembly 2 drafted 2026-10-06; Started 2026-08-18; the final decision waits on SCO-70            | Housing dimensions final      | Linear    |
| 4.9                                        | SCO-53                    | Revise the electronics housing cap for a cable gland                                        | John     | Phase 1 | In Progress      | 2026-08-16 | 2026-10-16 | 62 |                  | Gland placement follows the SCO-49 geometry; gland sizing and tolerance tests outstanding                                                     |                               | Linear    |
| 4.10                                       | SCO-107                   | Finish the electronics housing lid: bolt clearance holes and marking wording                | John     | Phase 1 | Todo             | 2026-10-12 | 2026-10-14 | 3  |                  |                                                                                                                                               |                               | estimated |
| 4.11                                       | SCO-103                   | Engrave the FCC ID label into the enclosure before printing                                 | John     | Phase 1 | Todo             | 2026-10-14 | 2026-10-16 | 3  | SCO-107          | Must precede the final print                                                                                                                  |                               | estimated |
| 4.12                                       | SCO-122                   | Order the stainless fasteners once the housing is dimensioned                               | John     | Phase 1 | Blocked          | 2026-10-16 | 2026-10-20 | 5  | SCO-49, SCO-70   | Vendor lead time; ordered after housing dimensions are final                                                                                  |                               | estimated |
| 4.13                                       | SCO-68                    | Design the chassis top section: sealing and service-access port                             | John     | Phase 1 | In Progress      | 2026-09-03 | 2026-10-16 | 44 |                  |                                                                                                                                               |                               | Linear    |
| 4.14                                       | SCO-75                    | Engineer the central chassis print structure for the mooring load path                      | John     | Phase 1 | In Progress      | 2026-08-21 | 2026-10-16 | 57 |                  |                                                                                                                                               |                               | Linear    |

|                                      |                                      |                                                                                                                |          |         |             |            |            |    |                 |                                                                                                      |                                     |           |
|--------------------------------------|--------------------------------------|----------------------------------------------------------------------------------------------------------------|----------|---------|-------------|------------|------------|----|-----------------|------------------------------------------------------------------------------------------------------|-------------------------------------|-----------|
| 4.15                                 | SCO-93                               | Print the chassis on the industrial printer                                                                    | John     | Phase 1 | In Progress | 2026-09-30 | 2026-10-16 | 17 |                 | Industrial printer window at work; about 35 hr print of the v5 design (later changes feed a reprint) | Chassis printed                     | Linear    |
| 4.16                                 | SCO-118                              | Get grad-student access to the Prusa XL in the garage                                                          | John     | Phase 1 | Todo        | 2026-10-06 | 2026-10-13 | 8  |                 | Needs a grad student's permission                                                                    |                                     | estimated |
| 4.17                                 | SCO-63                               | Bring the large lab 3D printer back online                                                                     | John     | Phase 1 | Backlog     | 2026-10-06 | 2026-10-16 | 11 |                 | Lab technician or advisor help                                                                       |                                     | Linear    |
| 4.18                                 | SCO-76                               | Run foam-fill manufacturing trials on sacrificial wedges                                                       | John     | Phase 1 | Todo        | 2026-10-13 | 2026-10-16 | 4  | SCO-118         | Printer access for sacrificial wedges                                                                |                                     | Linear    |
| 4.19                                 | SCO-123                              | Publish up-to-date v5 drawings for the wedge and wedge bottom                                                  | John     | Phase 1 | Todo        | 2026-10-12 | 2026-10-16 | 5  |                 |                                                                                                      |                                     | estimated |
| 4.20                                 | SCO-124                              | Rebuild the freeboard model's vertical stack from the STEP geometry                                            | John     | Phase 1 | In Progress | 2026-09-29 | 2026-10-12 | 14 |                 | v7 STEP committed 2026-10-06                                                                         |                                     | estimated |
| 4.21                                 | SCO-74                               | Build a mass budget and displacement/freeboard model                                                           | John     | Phase 1 | Blocked     | 2026-10-12 | 2026-10-14 | 3  | SCO-124, SCO-70 | Linear due 10-16; needs component masses from Isabella (SCO-70)                                      | Freeboard model complete            | estimated |
| 4.22                                 | SCO-80                               | Quantify stability: CG/CB, component placement, ballast provision                                              | John     | Phase 1 | In Progress | 2026-08-21 | 2026-10-16 | 57 | SCO-74          | Started 2026-08-21; final numbers follow the SCO-74 mass budget                                      |                                     | Linear    |
| 4.23                                 | SCO-73                               | Run FEA load cases LC1-LC9                                                                                     | John     | Phase 1 | Blocked     | 2026-10-14 | 2026-10-23 | 10 | SCO-74, SCO-135 |                                                                                                      |                                     | estimated |
| 4.24                                 | SCO-135                              | Re-run LC7 with the mooring moved to the pipe collar                                                           | John     | Phase 1 | Todo        | 2026-10-12 | 2026-10-14 | 3  | SCO-124         |                                                                                                      |                                     | estimated |
| 4.25                                 | SCO-125                              | Develop the self-righting ballast stem to 24 in below the keel                                                 | John     | Phase 1 | Todo        | 2026-10-16 | 2026-10-23 | 8  | SCO-80          | Lead ballast permit question (SCO-136)                                                               |                                     | estimated |
| 4.26                                 | SCO-136                              | Check whether lead ballast is acceptable under the reef permit                                                 | John     | Phase 1 | Todo        | 2026-10-12 | 2026-10-16 | 5  |                 | Permit authority answer                                                                              |                                     | estimated |
| 4.27                                 | SCO-137                              | Confirm the swivel, U-bolt and AS568-247 part numbers                                                          | John     | Phase 1 | Todo        | 2026-10-12 | 2026-10-14 | 3  |                 |                                                                                                      |                                     | estimated |
| 4.28                                 | SCO-77                               | Define the marine fastener and anti-loosening strategy                                                         | John     | Phase 1 | Backlog     | 2026-10-12 | 2026-10-16 | 5  |                 |                                                                                                      |                                     | Linear    |
| 4.29                                 | SCO-72                               | Identify a propeller-resistant mooring/tether line                                                             | John     | Phase 2 | Backlog     | 2026-10-19 | 2026-10-30 | 12 |                 |                                                                                                      |                                     | estimated |
| 4.30                                 | SCO-94 / 144 / 145 / 146 / 147 / 148 | Design improvement studies (inserts, cable routing, modular rod, split chassis, float-free, manufacturability) | John     | Phase 2 | Backlog     | 2026-10-26 | 2026-11-25 | 31 |                 |                                                                                                      |                                     | estimated |
| 4.31                                 | SCO-54 / SCO-56                      | Refine the stem and solar mount; audit the Onshape Initial Frame folder                                        | John     | Phase 2 | Backlog     | 2026-10-19 | 2026-11-25 | 38 |                 |                                                                                                      | Phase 2 mechanical exit             | Linear    |
| 4.32                                 | SCO-61 / SCO-66                      | Design the snap-connector sensor string; produce an exploded-view animation                                    | John     | Phase 2 | Backlog     | 2026-11-02 | 2026-11-25 | 24 |                 |                                                                                                      |                                     | Linear    |
| 4.33                                 | SCO-92 / SCO-64 / SCO-78 / SCO-79    | Corrosion strategy, material samples, marine coating, biofouling features                                      | John     | Phase 3 | Todo        | 2026-11-30 | 2027-01-15 | 47 | SCO-77          | Winter break; printer access                                                                         | Phase 3 exit                        | Linear    |
| 4.34                                 | SCO-81                               | Verify buoyancy under one-wedge-lost and chassis-flooded cases                                                 | John     | Phase 3 | Blocked     | 2026-11-30 | 2027-01-15 | 47 | SCO-74          |                                                                                                      |                                     | Linear    |
| <b>5 Deployment &amp; compliance</b> |                                      |                                                                                                                |          |         |             |            |            |    |                 |                                                                                                      |                                     |           |
| 5.1                                  | SCO-143                              | Identify a local backup test site and request pool access                                                      | John     | Phase 1 | Backlog     | 2026-10-12 | 2026-10-30 | 19 |                 | Site owner's permission                                                                              |                                     | estimated |
| <b>Milestones &amp; deadlines</b>    |                                      |                                                                                                                |          |         |             |            |            |    |                 |                                                                                                      |                                     |           |
| M2                                   | SCO-70                               | Component list delivered; unblocks housing dimensions                                                          | Isabella | Phase 1 |             | 2026-10-08 | 2026-10-08 | 1  |                 |                                                                                                      | Component list final                | Linear    |
| M1                                   |                                      | Bench parts arrive (assumed Fri)                                                                               | All      | Phase 1 |             | 2026-10-09 | 2026-10-09 | 1  |                 | Assumption; confirm with Isabella                                                                    | Parts arrive                        | estimated |
| M3                                   |                                      | Phase 1 exit: subsystem bring-up complete                                                                      | All      | Phase 1 |             | 2026-10-16 | 2026-10-16 | 1  |                 | Phase 1 project window                                                                               | Phase 1 exit                        | Linear    |
| D1                                   |                                      | SCU: Undergraduate Programs Project Funding Request due; Gantt chart due                                       | All      | Phase 1 |             | 2026-10-18 | 2026-10-18 | 1  |                 | SCU Senior Design Resources page                                                                     | Funding request and Gantt submitted | Linear    |
| M4                                   |                                      | Phase 2 starts: system integration                                                                             | All      | Phase 2 |             | 2026-10-19 | 2026-10-19 | 1  |                 |                                                                                                      |                                     | Linear    |
| M5                                   |                                      | Phase 2 exit                                                                                                   | All      | Phase 2 |             | 2026-11-25 | 2026-11-25 | 1  |                 |                                                                                                      | Phase 2 exit                        | Linear    |

|    |  |                                                            |     |         |  |            |            |   |  |                                  |              |        |
|----|--|------------------------------------------------------------|-----|---------|--|------------|------------|---|--|----------------------------------|--------------|--------|
| M6 |  | Phase 3 exit: enclosure and waterproofing                  | All | Phase 3 |  | 2027-01-15 | 2027-01-15 | 1 |  |                                  | Phase 3 exit | Linear |
| D2 |  | SCU: Senior Design Conference registration closes (winter) | All | Phase 4 |  | 2027-02-01 | 2027-02-01 | 1 |  | SCU Senior Design Resources page |              | Linear |

Date source: **Linear** = taken from the issue; **estimated** = proposed from the issue text, parts timing or the phase window and awaiting the owner's confirmation; **derived** = set by this assignment. Days are calendar days, inclusive.
